


2020 PAVEMENT REHABILITATION PROJECT

ACCEPTANCE OF THE CONSTRUCTION IMPROVEMENTS

APRIL 27, 2022

Attachment 3

PROJECT OVERVIEW

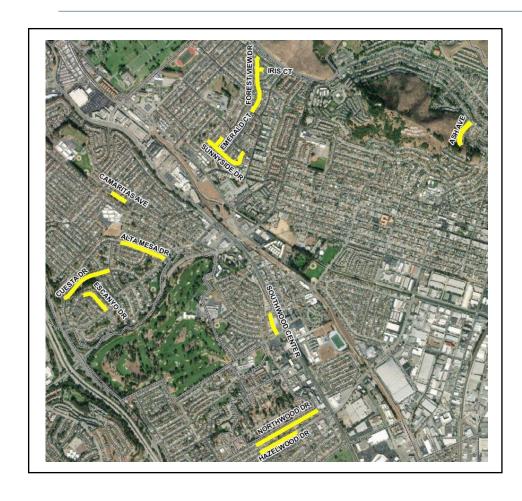

Street Segments

- Alta Mesa Drive Emeral Court,
- Ash Avenue Forestview Drive
- Camaritas Avenue Iris Court
- Cuesta Drive
- Sunnyside Drive
- Escanyo Drive
- Keats Ave
- Hazelwood Drive
- Ryan Way
- Northwood Drive
- Southwood Center

Emerald Dr and Sunnyside Dr – Hot Mix Asphalt Overlay






Holly Ave and Sunnyside Dr – Hot Mix Asphalt Overlay / High Visibility Crosswalks






Los Flores Ave and Camaritas Ave – Valley Gutter Repair / Hot Mix Asphalt Overlay

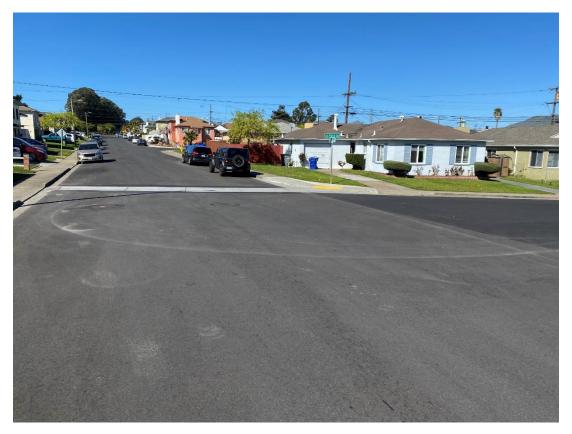



Hazelwood Dr – ADA Compliant Ramps / Hot Mix Asphalt Overlay / High Visibility Markings

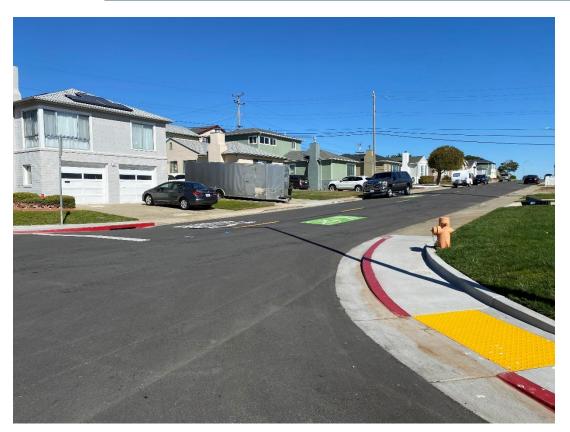



CONSTRUCTION COST

The total construction cost incurred for the project is summarized as follows:

	Project Budget	Actual Costs
Bay Cities Paving & Grading Inc – Construction Contract	\$2,541,450.00	\$2,541,450.00
Construction Contingency (20% projected versus 3% actual)	\$508,290.00	\$79,290.90
Total Construction Budget / Costs	\$3,049,740.00	\$2,620,750.90

QUESTIONS?
